
Calira

Formerly Clustermarket

Enterprise equipment scheduling for Charles River Laboratories

Proposal summary · 2026

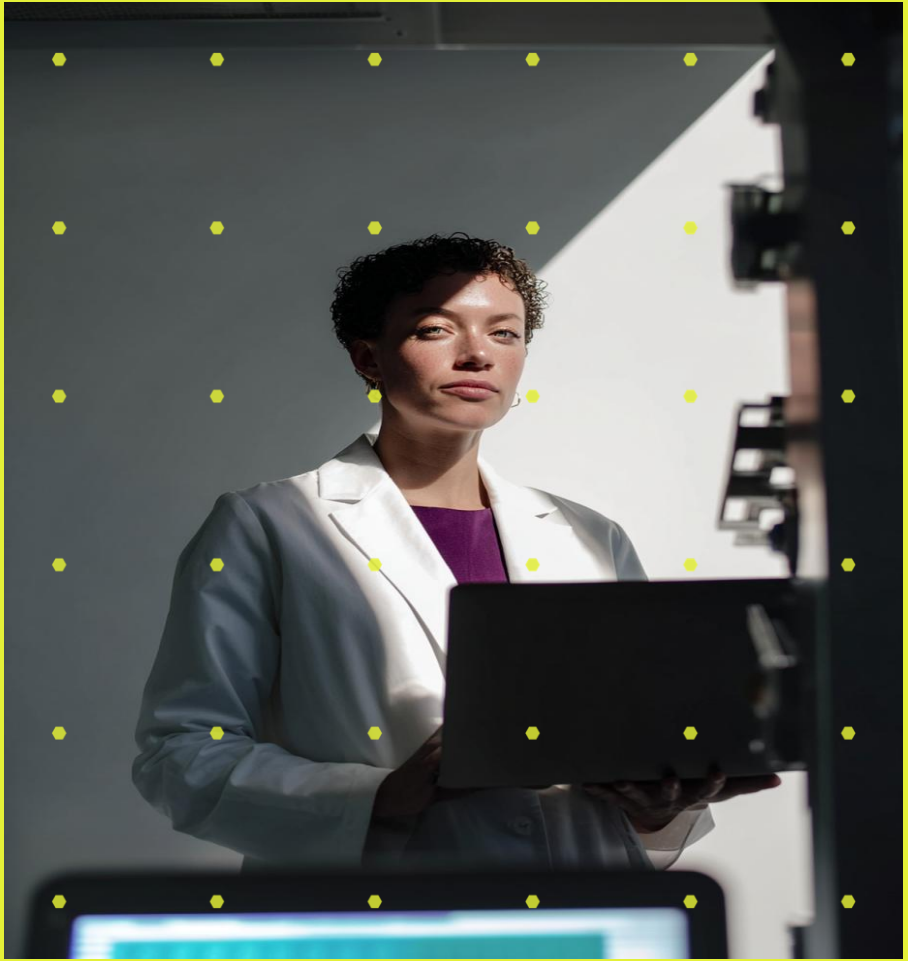

Craig Davison
Senior Account Executive, Calira
craig@calira.co

© 2026 calira.co All rights reserved

AGENDA

What we will cover in the next 25 minutes

Structured around the six areas you asked us to focus on

1	**Calira in brief** Who we are, scale, and our existing work inside CRL	3 min
2	**Your objectives and challenges** What we heard, and how we read your requirements	4 min
3	**Proposed solution** Key capabilities, scalability, and – candidly – the constraints	6 min
4	**Differentiators and value drivers** Why Calira, and where the value comes from	4 min
5	**Implementation approach** Lead site in 8 weeks, then rollout waves; team and KPIs	4 min
6	**Commercial, licensing and cost structure** Licence model, services, terms and exceptions	3 min



ABOUT CALIRA

Built for R&D at scale – and already live inside CRL

The world's leading R&D equipment scheduling platform · founded 2019 · rebranded from Clustermarket in 2025 · London, Sofia, Boston

11M+	84,000+	66,000+	1,800+	50+
bookings	active users	instruments	laboratories	countries

Trusted by leading life-science organisations

Already a CRL partner

- Live today in CRL's Chemistry department, Edinburgh, under an existing contract
- Day-to-day equipment scheduling plus insight into asset utilisation, revenue per asset and analysis success rates
- 16 enterprise implementations of 500+ users as primary implementer; multi-site rollouts at Novo Nordisk, Moderna and Eli Lilly
- Year-on-year growth of 81% (2024–25) and 34% (2025–26); 17 staff, 9 in product and engineering

YOUR OBJECTIVES

What we heard: one enterprise scheduling method, with evidence you can act on

Your strategic objective

A unified, enterprise-scale platform that accelerates study delivery, optimises resource allocation and enables data-driven decisions – replacing a patchwork of local applications and shared spreadsheets with a single source of truth for planning, scheduling and execution.

Your requirements span eight areas

Core scheduling · User experience · Governance · Integration · Global planning · Functional scheduling · Tasking · Execute & adjust

The scheduling challenges behind it

1. **Local and inconsistent**
   Scheduling is run site by site, in different tools and spreadsheets, with no common method.

2. **Capacity you cannot see**
   Instrument capacity is invisible at enterprise level, so it cannot be planned or shared across sites.

3. **Time lost to coordination**
   Scientists and lab managers spend effort negotiating access manually; conflicts delay studies.

4. **Capital decisions without evidence**
   Purchase, relocation and retirement decisions are taken without reliable utilisation data.

SOLUTION

Provantis runs the study; Calira runs the resources

Our honest position on scope – stated openly in the C1 questionnaire and reflected in the SOW

Study layer – Provantis, RPM, Apollo (CRL systems)

Study award to finalisation · milestones, endpoints and deliverables · protocols and study types · staffing and animal resources · portfolio and programme planning

REST API · discovery-gated integration

Resource layer – Calira

- Equipment, rooms and specialised resources scheduled to the minute, across sites and time zones (UTC-stored)
- Booking rules, approvals, access groups and training-based access; recurring, group and multi-step workflow bookings
- Actual usage captured at the instrument (LabTrack) and at the point of use (Custom Forms)
- Utilisation, capacity and adoption data for every lab, department and site – exportable and API-accessible

What Calira does not do today


- Model studies or milestones, or generate schedules from them
- Schedule people or animals, or integrate HR, leave and skills data
- Automatically re-plan, cascade dependencies or optimise by weighting factors
- Gantt or study-calendar views; scheduled exports (CSV and API exports are supported)
- A complete 21 CFR Part 11 audit trail across all scheduling actions (on our roadmap) or GxP validation deliverables

Why this is the right split. It keeps the study system of record where it already is, avoids duplicating Provantis, lowers total cost of ownership and lets CRL adopt the resource layer in weeks rather than years.

SOLUTION

Requirement fit: strongest where scheduling meets the bench

Tally of our 73 responses in Exhibit C1 (Solution Requirements Questionnaire)

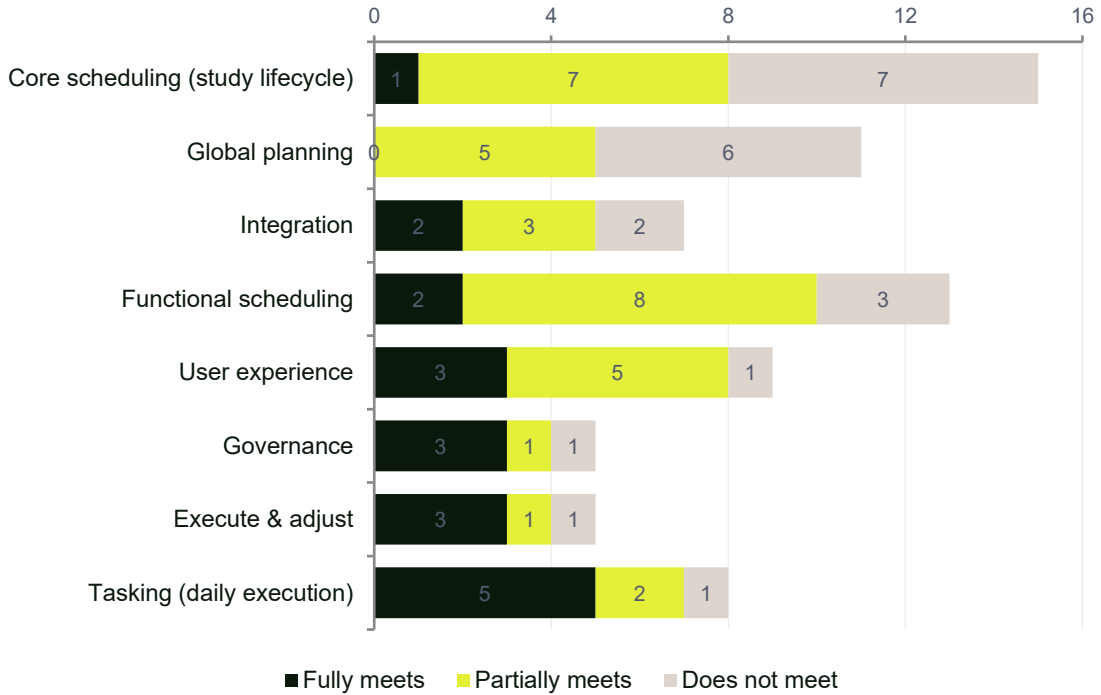

Strong fit

Functional scheduling, tasking, execute & adjust, governance and user experience: the day-to-day of booking, using and reporting on shared resources.

Partial fit

Global planning: multi-site utilisation and capacity views are native; study, portfolio and scenario modelling are not.

By design, not a gap

Study-lifecycle scheduling stays in Provantis. Calira supplies the resource availability and actuals it needs.

SOLUTION

What CRL gets on day one

Configured, not custom-built – every capability below is standard product



Book and schedule

- Drag-and-drop calendar, 15-minute slots
- Rules, quotas, cut-offs and approvals
- Recurring, group and workflow bookings



Equipment estate

- Bulk registration, metadata, documents, SOPs
- Rooms, parent/child equipment, locations
- Maintenance, service contracts and alerts



Access and governance

- SAML 2.0 SSO, MFA, joiner/mover/leaver
- Seven roles plus access groups
- Training-based access; per-lab time zones



Capture at the point of use

- Custom Forms: results, sample IDs, files
- LabTrack: actual usage and instrument locking
- Live instrument status via the OEM Gateway



Report and extract

- Reports module, saved filters, CSV export
- Read/write REST API (OAuth2)
- Metabase dashboards at no extra cost; optional AI assistant



Connect

- Outlook / Exchange calendar sync
- Benchling, eLabNext, RSpace; Essentim sensors
- Provantis, Maximo, Sapio via discovery-gated adapters

SOLUTION

Built to run enterprise-wide: scale, resilience and security

Scale

- Multi-tenant SaaS on AWS (Dublin), containerised on Kubernetes
- Horizontal and vertical auto-scaling – no licence impact when scaling
- 1,800+ labs in 50+ countries; per-lab time zones with UTC storage
- Named-user licensing with unlimited instruments and sites
- Responsive web app on desktop, tablet and mobile; no client install (LabTrack optional, Windows)

Resilience

- Components across multiple availability zones; RDS with standby and automated failover
- Continuous point-in-time recovery (96 h), daily and weekly backups, encrypted and off-site
- Availability target 99.8% per month; SLA with service credits; status.calira.co
- 24/7 monitoring (Grafana, Prometheus, Sentry, Coralogix, UptimeRobot); P1 response 30 min
- Zero-downtime CI/CD releases; DR restore within 24 h

Security

- Cloudflare WAF, DDoS protection and rate limiting at the edge; database reachable only inside the private network
- TLS 1.2+ in transit, AES-256 at rest; secrets in KMS
- SSO (SAML 2.0), MFA, least-privilege RBAC, quarterly access reviews
- Hosting partner ISO 27001 and Cyber Essentials Plus; annual penetration test
- GDPR-compliant, EEA-hosted; AI features can be disabled at account level

Hosting partner: ISO 27001 & Cyber Essentials Plus

Annual penetration test · quarterly vulnerability scans


GDPR · EEA-hosted · DPA with SCCs

Public status page: status.calira.co

SOLUTION

Integrations: two standard, three discovery-gated

You see each Discovery Report – and decide – before any integration build is priced

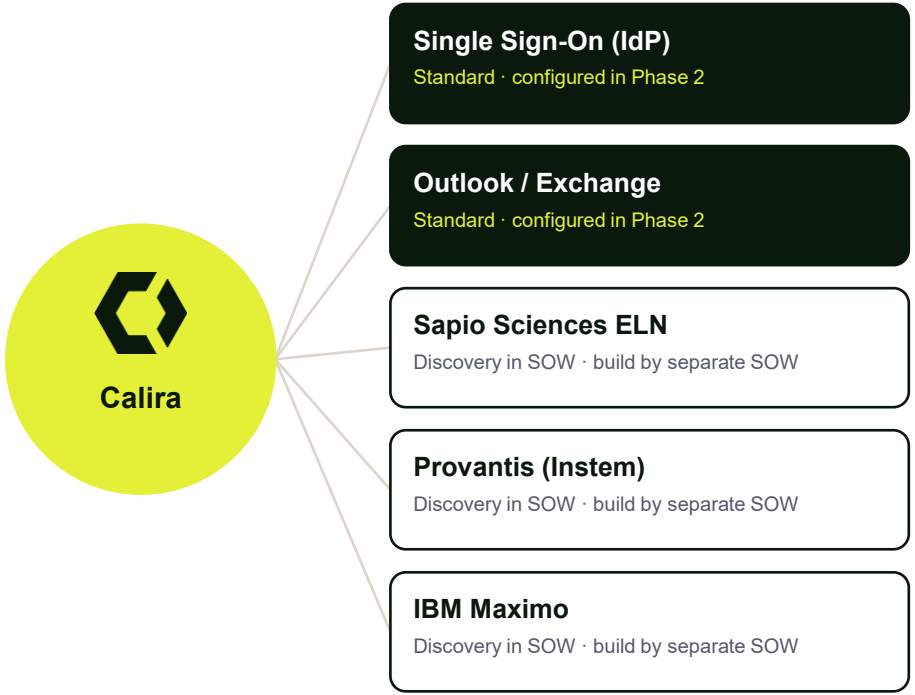

Why we are confident on the three new systems

- One adapter framework for every integration: OAuth2/API-key auth, signed webhooks, background processing, central monitoring – a new vendor is a new adapter, not new infrastructure
- Provantis: our Head of Product spent 5+ years at Instem and knows the module architecture; Instem's new REST API and hosted SaaS delivery fit our pattern
- Maximo: enterprise-asset data mapping already scoped for Blue Mountain RAM; Maximo Manage REST API is mature and documented
- Sapio: live ELN integrations with Benchling and eLabNext follow the same REST-plus-webhook shape
- Each discovery ends in a report with data mapping, auth approach, dependencies and a build estimate – accepted by CRL before any build SOW

DIFFERENTIATORS

Why Calira for CRL

Six things we would ask you to weigh against any alternative

Proven inside CRL

Live in Edinburgh Chemistry under an existing contract – a reference you can call today, and a configuration baseline we can reuse.

Speed to value

Lead site live in 8 weeks; each further site faster against the baseline. Standard implementation carries no services fee.

Adoption by design

Researchers productive after 20–30 minutes of training; mobile and QR-code booking; contractual adoption KPIs.



Actuals, not assumptions

LabTrack records real instrument sessions and locks equipment to bookings, so utilisation is measured, not guessed.



AI-native, optional

Natural-language querying and anomaly detection over usage data – switchable off at account level if CRL prefers.



A partner, not a ticket queue


Named Solutions Manager through go-live, named Customer Success Manager after it, product leadership in the room.

VALUE DRIVERS

The value case: utilisation, time and capital

35%

average utilisation of R&D lab equipment – mostly lost to short, unmanaged stoppages (McKinsey, 2021)

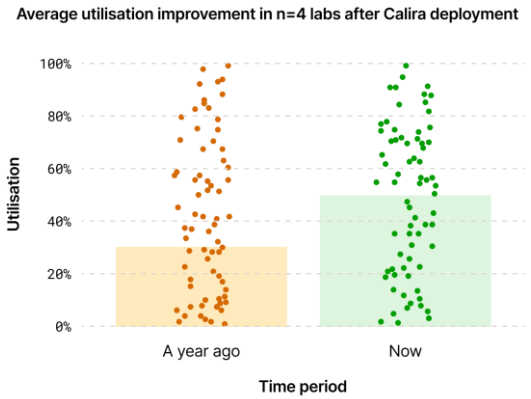

Fewer conflicts, less coordination

One live calendar per resource with rules and approvals removes double-booking and the negotiation around it.

Higher utilisation, deferred capital

Visibility plus measured actuals raise use of existing instruments before new ones are bought.

Enterprise capacity you can plan

Utilisation and capacity rolled up across labs, departments and sites – shared, moved or retired on evidence.

A single source of truth

Bookings, actual usage, maintenance and point-of-use records in one auditable place, exportable and API-accessible.


Lower total cost of ownership

Configuration not customisation, no implementation fee, and best-of-breed integration rather than replacing Provantis.

IMPLEMENTATION

Lead site live in 8 weeks, then rollout waves

Three concurrent workstreams under our four-phase enterprise onboarding methodology

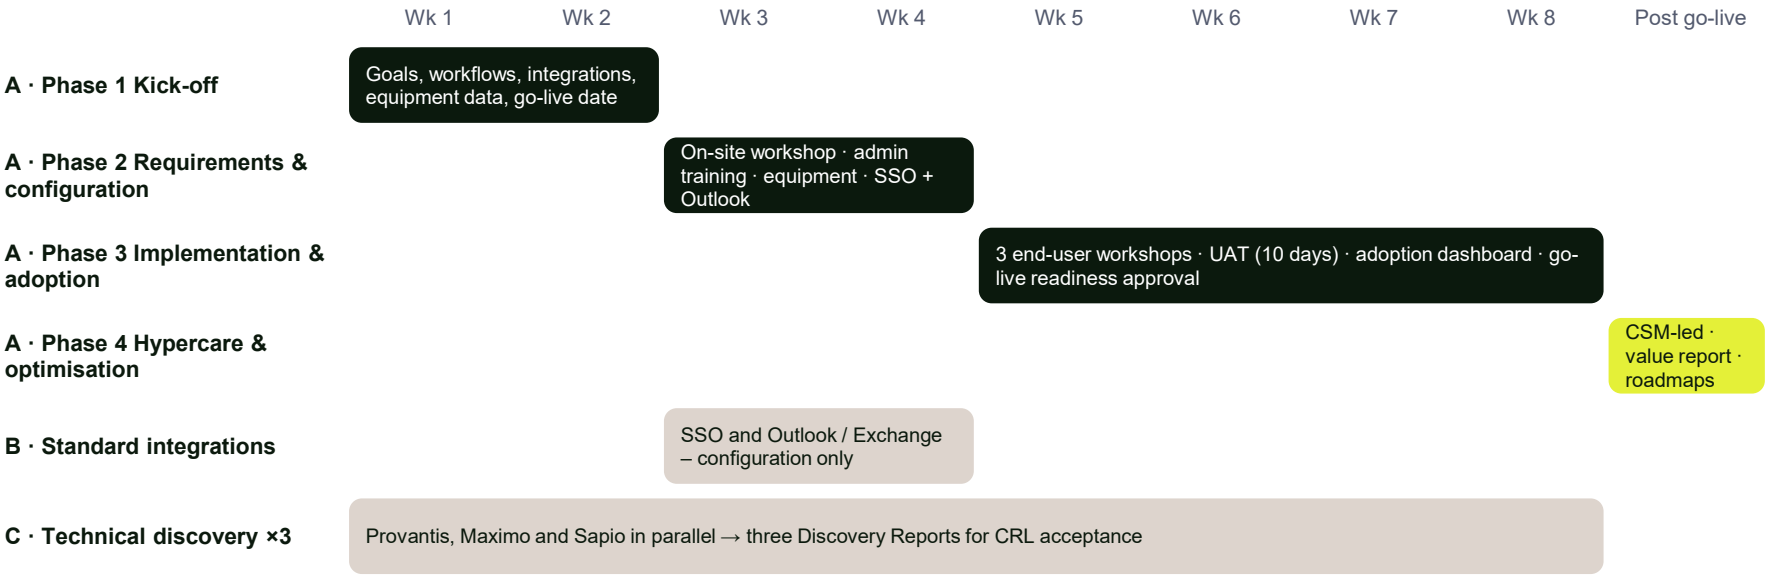

Rollout waves. Each further site is onboarded against the Lead Site's configuration baseline, workflow library and training curriculum: Phase 1 reduced to site-specific confirmation, Phases 2–3 in full (on-site workshop per qualifying site), Phase 4 once at enterprise level. Sites are sequenced so each wave learns from the last.

IMPLEMENTATION

Your Calira team, and the adoption KPIs we sign up to

MA **Morsal Amini**
Senior Solutions Manager · implementation lead, Phases 1–3 and all waves

NB **Nathan Beynon**
Customer Success Manager · Phase 4 hypercare, adoption and value reporting

CM **Chris Mills**
Head of Product · project manager; 25 years in R&D software, formerly Instem

HT **Hristo Tenev**
Integration Engineer · Provantis, Maximo and Sapio discovery and build

CD **Craig Davison**
Senior Account Executive · commercial lead and escalation

From CRL: project owner, IT (SSO, integrations), lab managers and admins, early-adopter users. All Calira staff are full-time employees; no implementation partner.

KPI	Target	If missed
Workshop attendance	≥ 80% of invited SMEs per site	Extra virtual workshop, no fee
Administrator coverage	100% attend a training session	Extra admin session, no fee
Training coverage	100% of named users trained	Go-live not sought until remedied
User activation	≥ 75% accept invitation within 10 days	Adoption clinic + mitigation plan
Booking adoption	≥ 50% of activated users book within 30 days	Support workshop + workflow review
Sustained adoption	≥ 50% of users active monthly, 3 months	Further optimisation support
Discovery quality	Reports accepted without material rework	Revised and resubmitted, no fee

Measured from the adoption dashboard and reported at each check-in; targets assume CRL releases users for training.

COMMERCIALS

Named users, unlimited instruments, no implementation fees

Headline figures from Exhibits D1A, D2a/b and the SOW – all list prices in USD

Licence

- Named-user annual subscription: $405 per user per year (list)
- Unlimited instruments, rooms, sites and bookings
- Volume tiers: 10% off from 501 users, 15% from 1,001, 20% from 1,501, 25% from 2,001 (applied per tier band)
- Multi-year: 10% off for 3 years, 15% for 5 years
- LabTrack real-time tracking optional: $140 per asset per year
- Site or enterprise licence available – open to discussion

Services

- Core implementation, training, SSO and Outlook: $0 (100% discount on standard implementation services)
- Technical discovery for Provantis, IBM Maximo and Sapio: $31,200 fixed (30 engineer days + project management)
- Integration builds priced by separate SOW after CRL accepts each Discovery Report
- Initial SOW capped at $40,000 not-to-exceed
- On-site workshops: no fee; travel and accommodation at cost, pre-approved
- Rate card locked for the term

Terms

- Pricing locked for 3 years; two further 1-year extensions on the same terms, increases capped to an agreed index
- Users added any time, pro-rata, co-terminating with the annual term; re-baseline up or down at each anniversary
- Payment 60 days from invoice (90 available if helpful)
- SLA: availability with service credits; 10% of monthly fees at risk; termination for persistent failure
- Global, non-exclusive term licence covering CRL and affiliates

COMMERCIALS

Commercial principles: 26 of 30 agreed, four flagged openly

Exhibit C6 responses, which are contractually binding

Agreed

- 3-year price lock, two 1-year extensions, index-capped increases
- Own resources for implementation and future services – no implementation partner
- User-based licensing; global, non-exclusive term licence for CRL and affiliates
- Ramp-up volumes, pro-rata additions, co-termination, annual re-baselining
- 60-day payment terms; rates locked for the term
- 99.5% uptime commitment, SLA credits, 10% of fees at risk, termination for persistent failure
- Proactive CX metrics, innovation tracking and demonstrable Agile delivery

Where we said no, or qualified our answer

GxP compliance

Calira is not GxP-validated; validation deliverables (IQ/OQ/PQ, Part 11) are excluded from the SOW. CRL may validate the platform itself.

Retroactive tier pricing

Tier discounts apply to users within each band, not to all users once a band is reached.

Credits for inactive users

Annual named-user contracts; users can be removed at any date, but no monthly-activity credit.

Partial termination

Termination rights are in whole, not by service line or geography.

NEXT STEPS

From proposal to lead-site go-live

1

References and demo

Reference calls with Novo Nordisk, Moderna, Eli Lilly and CRL Edinburgh; a hands-on demo against your workflows.

2

Confirm scope

Lead site, user and equipment counts, wave sequence and the integration priorities for discovery.

3

Contract and kick-off

MSA, SOW and DPA finalised; project owner nominated; go-live date set at the kick-off meeting.

4

Week 8

Lead site live and accepted; three Discovery Reports delivered; expansion plan agreed.

Questions

We are happy to walk through any individual requirement response, the SOW, or the security and architecture questionnaires.

Calira

Formerly Clustermarket

Thank you



Craig Davison · Senior Account Executive
craig@calira.co · +44 (0)75 4515 2687
Chris Mills · Head of Product · chris@calira.co
Clustermarket Ltd DBA Calira · 34 Lime Street, London EC3M 7AT
calira.co

© 2026 calira.co All rights reserved
